MERRILL, RICHARD

SUBMIT THE FOLLOWING COMPLETED FORM TO YOUR LOCAL PLUMBING INSPECTOR

DATE 8/13/72 & 8/14/72 NUMBER OF BEDROOMS Two SIZE OF SEPTIC TANK 750 gal. TYPE OF SOIL [illegible]	OWNER [illegible] STREET RFD #2 [illegible] CITY [illegible] MAINE TEL. NUMBER [illegible]
Test Performed by [illegible] [illegible] ME #1722	LOCATION OF PROPOSED INSTALLATION STREET [illegible]
Local Plumbing Inspector's Signature [illegible] 8/12..72.	CITY MAINE TEL. NUMBER

SKETCH: LOCATION OF BUILDING DISPOSAL SYSTEM, TERRAIN FEATURES, PERCOLATION HOLES, WATER SUPPLIES, ETC.

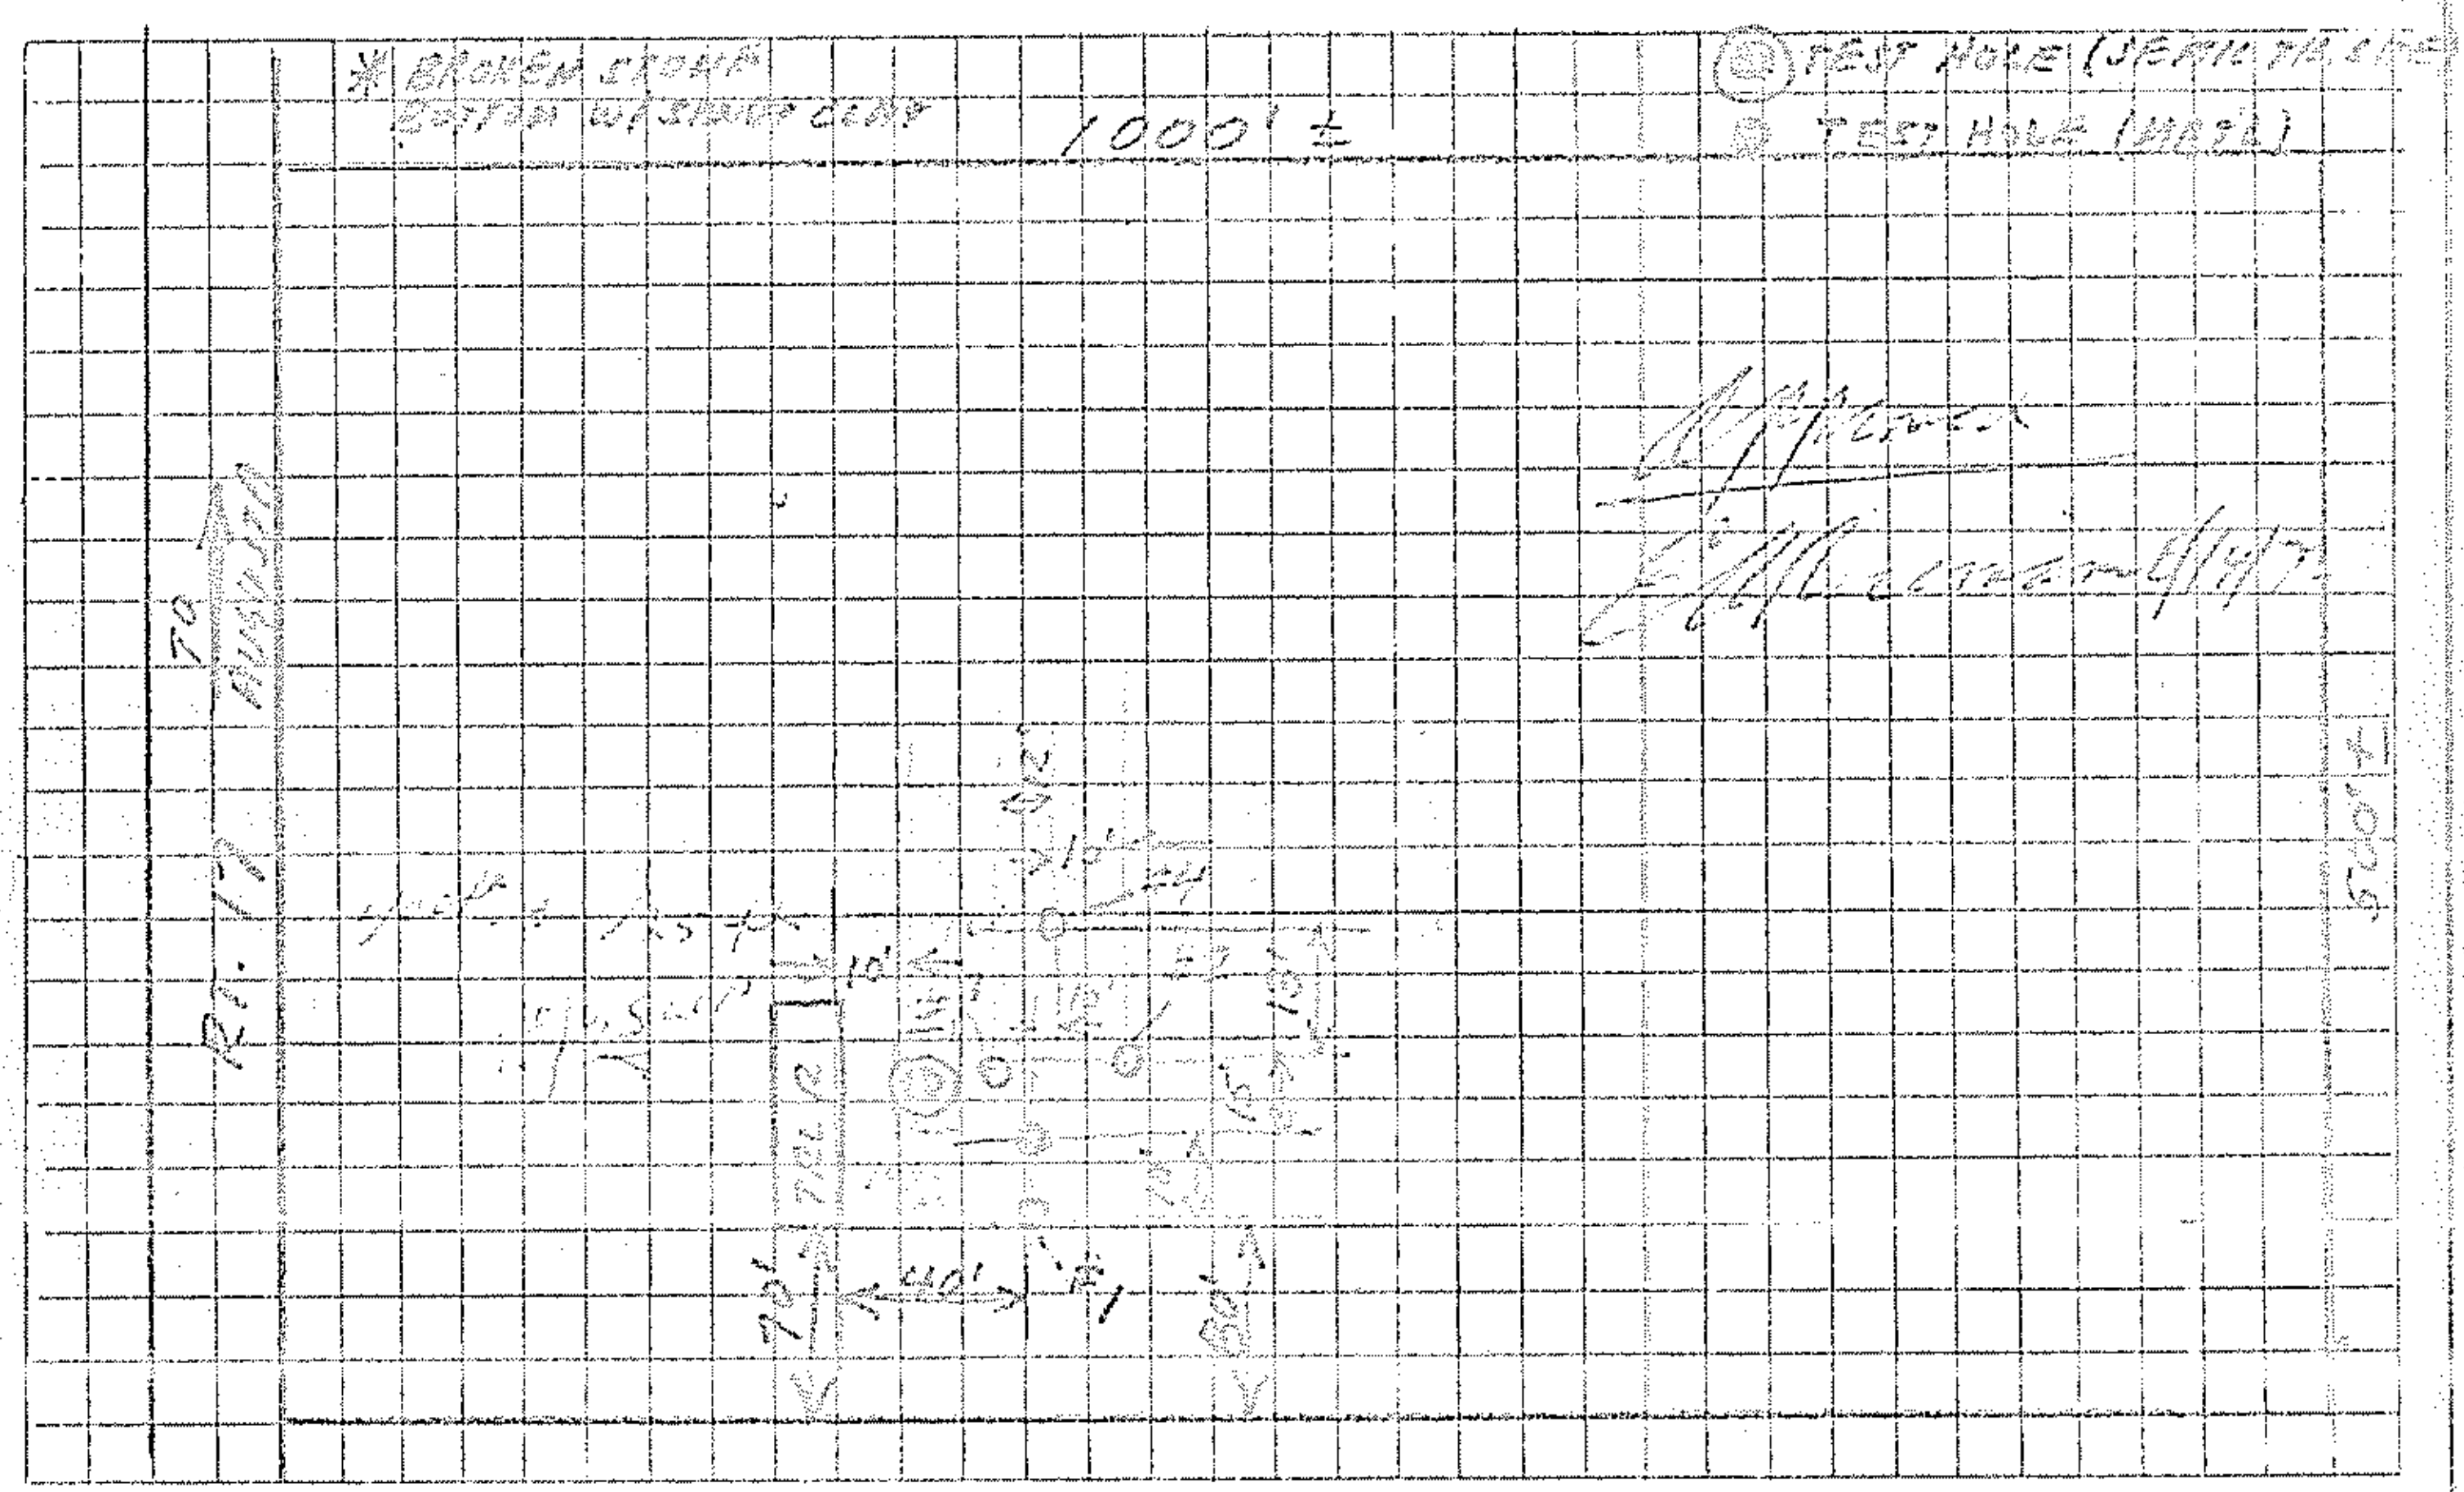

None Depth to Water Table
None Depth to Bedrock
None Depth to Clay or other impervious strata

REMARKS [illegible]

HOLE	HOLE DEPTH	TIME		DEPTH OF WATER SURFACE		ELAPSED TIME	TOTAL DROP OF WATER	PERCOL. RATE MINUTES/INCH
		START	FINISH	START	FINISH			
#1	38 in.	0610	0734	32 in.	36 in.	84 min.	4 in.	21 min/in
* #2	28 in.	0612	0726	22 in.	26 in.	74 min.	4 in.	18.5 min/in
#3	36 in.	0615	0733	29 in.	33 in.	78 min.	4 in.	19.5 min/in
#4	48 in.	0627	0732	41 in.	45 in.	65 min.	4 in.	16.3 min/in
						AVERAGE RATE		18.9 min/in

MERRILL, RICHARD

SUBMIT THE FOLLOWING COMPLETED FORM TO YOUR LOCAL PLUMBING INSPECTOR

DATE 8/13/72 & 9/14/72
NUMBER OF BEDROOMS Two
SIZE OF SEPTIC TANK 750 gal.
TYPE OF SOIL Sandy gravelly loam w/some clay

OWNER Richard Merrill
STREET Rte 42 - near Oxford Lake
CITY Buckfield MAINE
TEL. NUMBER 336-7771

Test Performed by Richard Merrill
Ernest R. Gibson HE #1722

Local Plumbing Inspector's Signature
C. J. Morton 8/12-72.

LOCATION OF PROPOSED INSTALLATION
STREET Above Hamlin
CITY MAINE
TEL. NUMBER

SKETCH: LOCATION OF BUILDING DISPOSAL SYSTEM, TERRAIN FEATURES, PERCOLATION HOLES, WATER SUPPLIES, ETC.

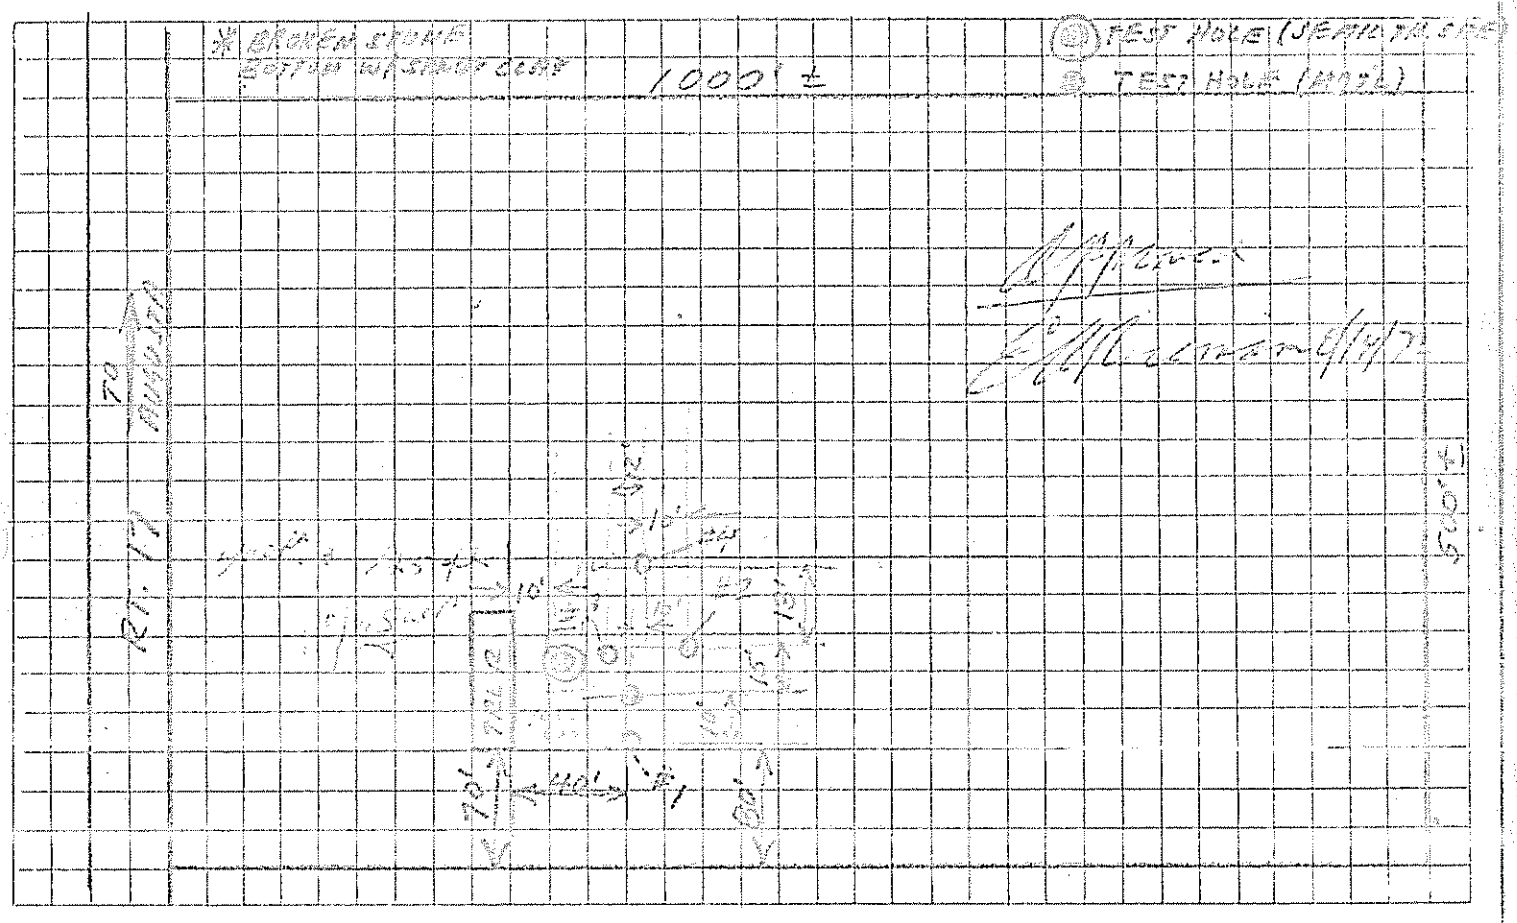

20 feet Depth to Water Table
None Depth to Bedrock
None Depth to Clay or other impervious strata

REMARKS Site approved well sited for a septic system well should be placed as southerly as possible in order of further drainage problem [illegible]

HOLE	HOLE DEPTH	TIME START	TIME FINISH	DEPTH OF WATER SURFACE START	DEPTH OF WATER SURFACE FINISH	ELAPSED TIME	TOTAL DROP OF WATER	PERCOL. RATE MINUTES/INCH
#1	38 in.	0610	0734	32 in.	36 in.	84 min.	4 in.	21 min/in
* #2	28 in.	0612	0726	22 in.	26 in.	74 min.	4 in.	18.5 min/in
#3	36 in.	0615	0733	29 in.	33 in.	78 min.	4 in.	19.5 min/in
#4	48 in.	0627	0732	41 in.	45 in.	65 min.	4 in.	16.3 min/in
						AVERAGE RATE		18.9 min/in

C. J. Morton
